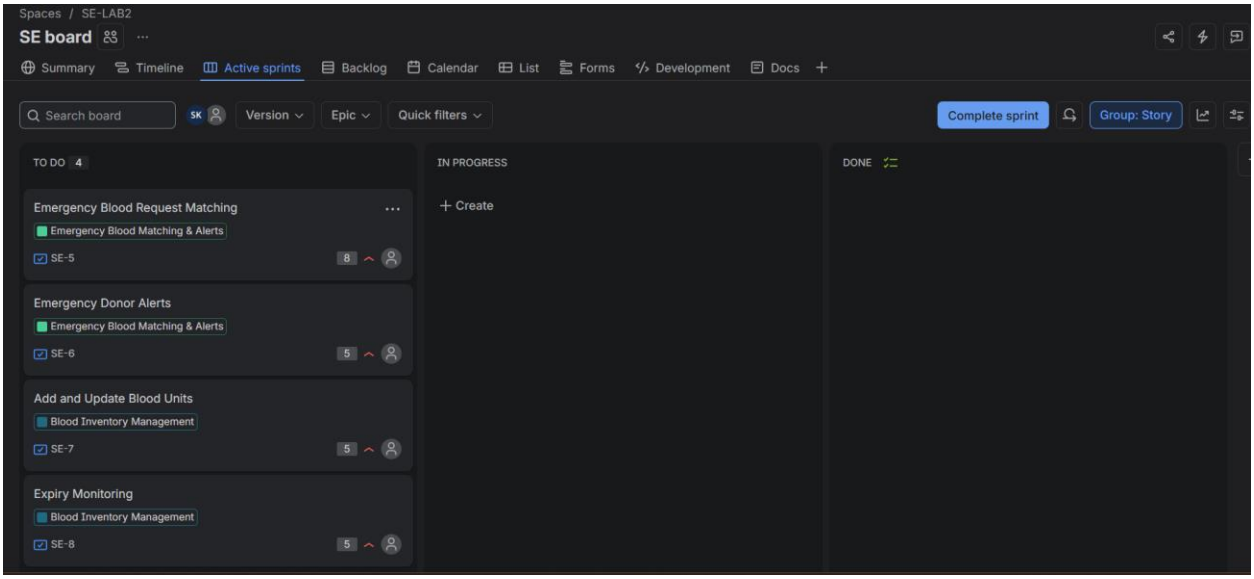
# SOFTWARE ENGINEERING-LAB 2

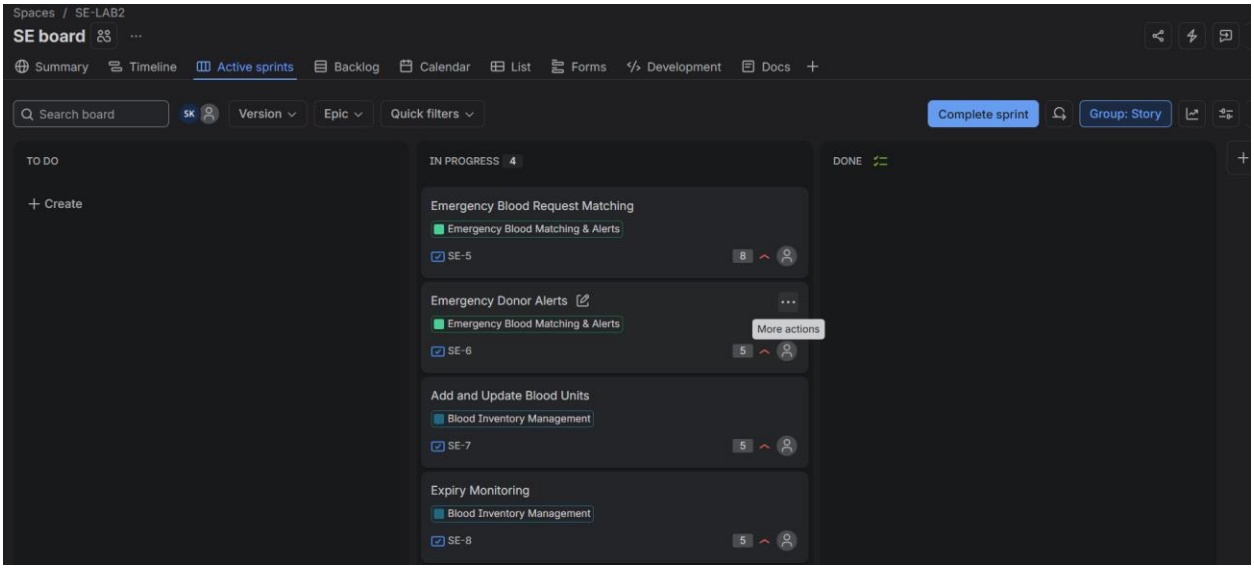
NAME: K SRUJANA

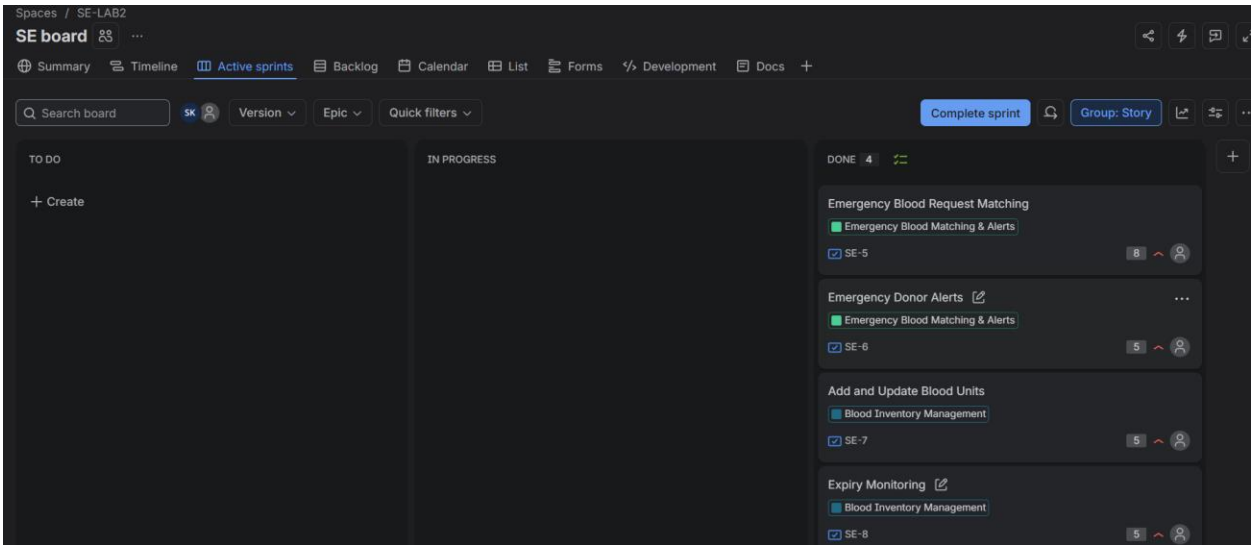
SRN: PES1UG24AM128

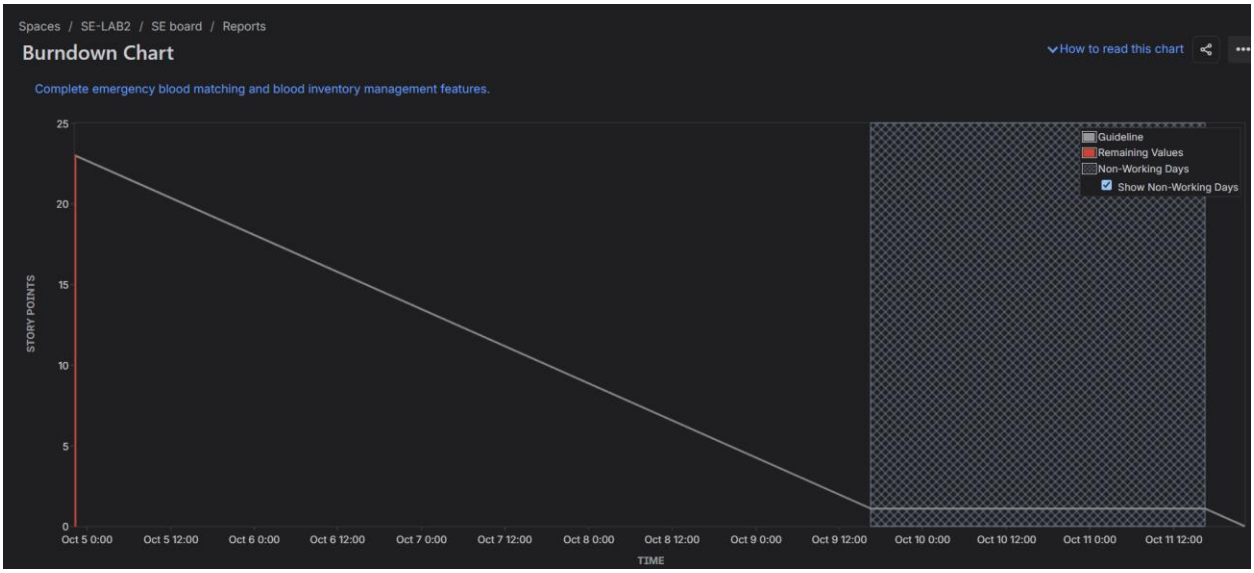
SEC: C

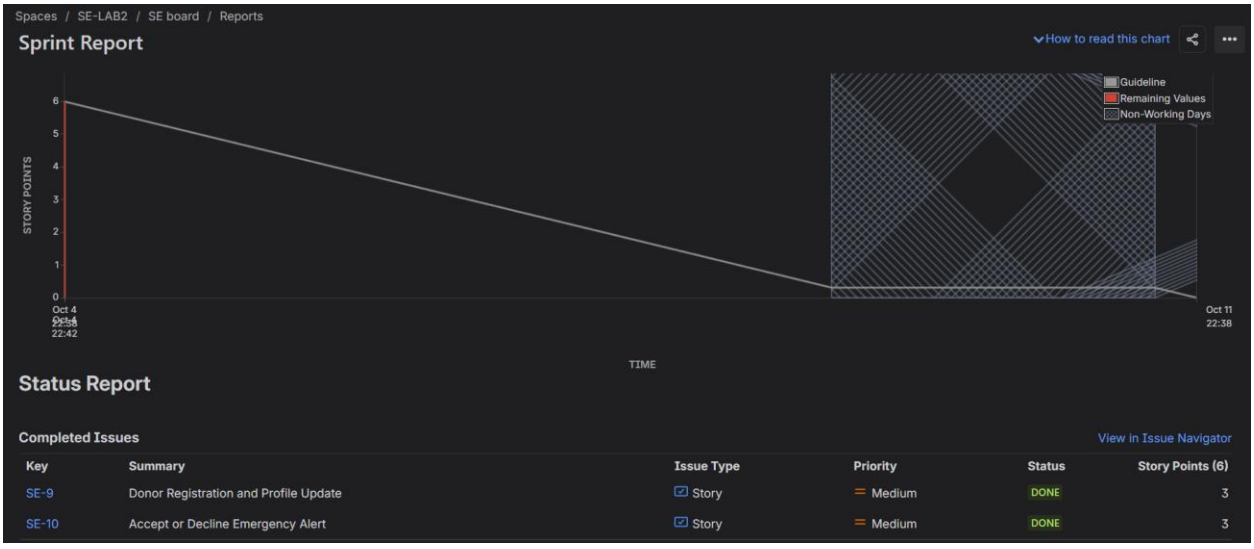
**SPRINT-1:**



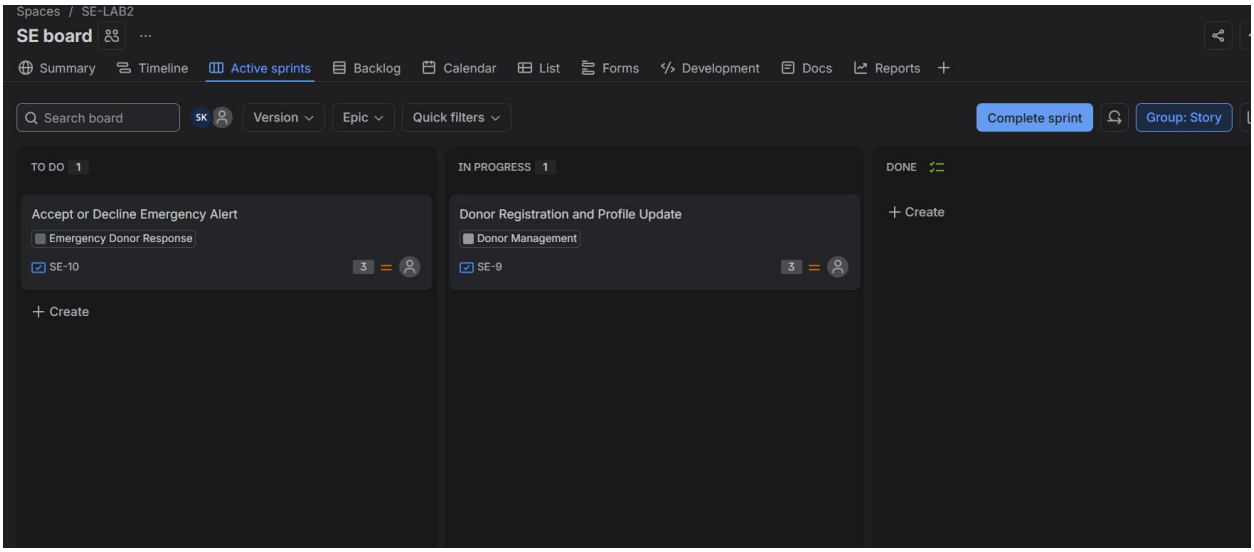



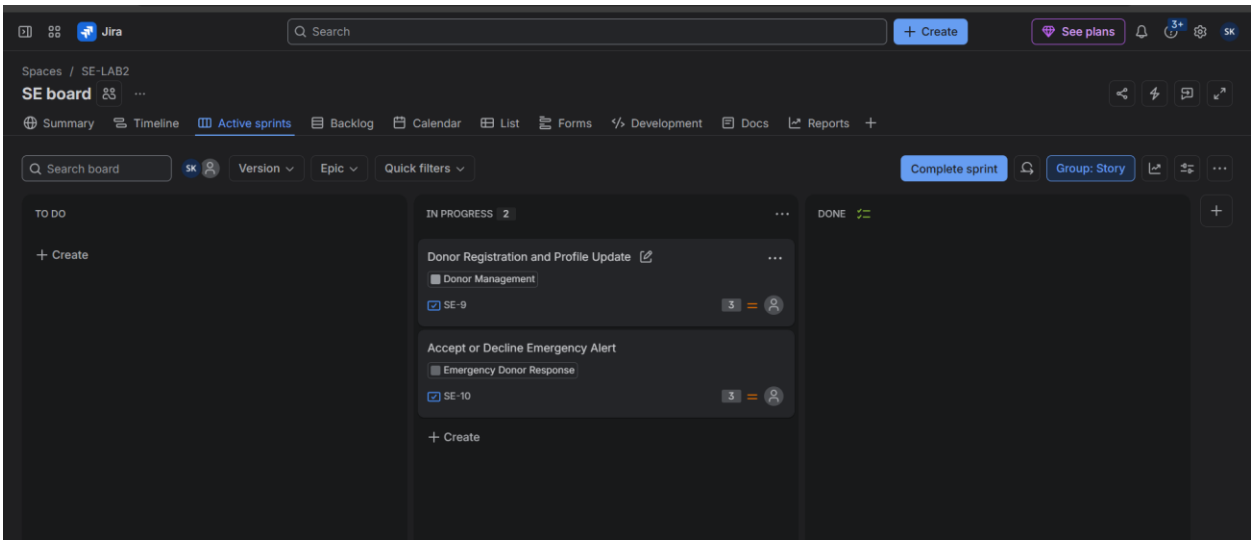

Spaces / SE-LAB2
SE board
Summary
Timeline
Active sprints
Backlog
Calendar
List
Forms
Development
Docs
Search board
Version
Epic
Quick filters
Complete sprint
Group: Story
TO DO
+ Create
IN PROGRESS
DONE 4
Emergency Blood Request Matching
Emergency Blood Matching & Alerts
SE-5
8
Emergency Donor Alerts
Emergency Blood Matching & Alerts
SE-6
5
Add and Update Blood Units
Blood Inventory Management
SE-7
5
Expiry Monitoring
Blood Inventory Management
SE-8
5

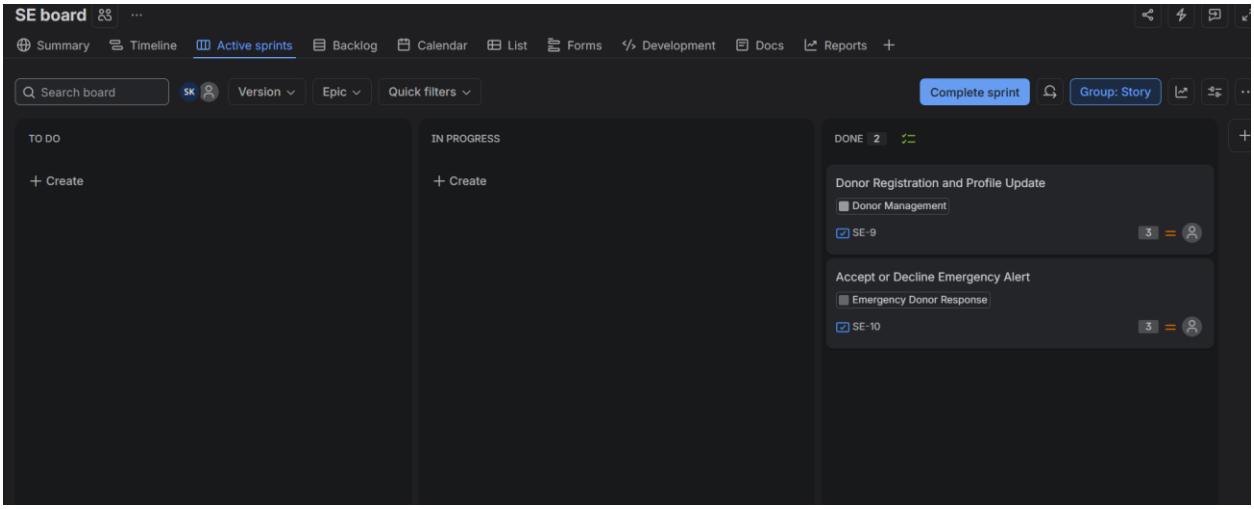

Spaces / SE-LAB2 / SE board / Reports
Burndown Chart
How to read this chart
Complete emergency blood matching and blood inventory management features.
STORY POINTS
25
20
15
10
5
0
Oct 5 0:00
Oct 5 12:00
Oct 6 0:00
Oct 6 12:00
Oct 7 0:00
Oct 7 12:00
Oct 8 0:00
Oct 8 12:00
Oct 9 0:00
Oct 9 12:00
Oct 10 0:00
Oct 10 12:00
Oct 11 0:00
Oct 11 12:00
TIME
Guideline
Remaining Values
Non-Working Days
Show Non-Working Days


Spaces / SE-LAB2 / SE board / Reports
Sprint Report
How to read this chart
STORY POINTS
6
5
4
3
2
1
0
Oct 4
22:42
Oct 11
22:38
TIME
Guideline
Remaining Values
Non-Working Days
Status Report
Completed Issues
View in Issue Navigator
Key
Summary
Issue Type
Priority
Status
Story Points (6)
SE-9
Donor Registration and Profile Update
Story
Medium
DONE
3
SE-10
Accept or Decline Emergency Alert
Story
Medium
DONE
3

## SPRINT-2:


Spaces / SE-LAB2
SE board
Summary
Timeline
Active sprints
Backlog
Calendar
List
Forms
Development
Docs
Reports
Search board
Version
Epic
Quick filters
Complete sprint
Group: Story
TO DO 1
IN PROGRESS 1
DONE
Accept or Decline Emergency Alert
Emergency Donor Response
SE-10
Donor Registration and Profile Update
Donor Management
SE-9
Create


Jira
Search
Create
See plans
Spaces / SE-LAB2
SE board
Summary
Timeline
Active sprints
Backlog
Calendar
List
Forms
Development
Docs
Reports
Search board
Version
Epic
Quick filters
Complete sprint
Group: Story
TO DO
IN PROGRESS 2
DONE
Create
Donor Registration and Profile Update
Donor Management
SE-9
Accept or Decline Emergency Alert
Emergency Donor Response
SE-10


SE board
Summary
Timeline
Active sprints
Backlog
Calendar
List
Forms
Development
Docs
Reports
Search board
Version
Epic
Quick filters
Complete sprint
Group: Story
TO DO
IN PROGRESS
DONE 2
Create
Donor Registration and Profile Update
Donor Management
SE-9
Accept or Decline Emergency Alert
Emergency Donor Response
SE-10




**QUESTIONS:**

1. Did your estimations reflect the actual effort?

The story points were estimated using the Fibonacci scale based on the relative complexity, effort, and uncertainty of each requirement. Sprint 1 contained 4 user stories with a total of 21 story points, while Sprint 2 contained 3 stories with a total of 16 story points.Since this was a simulated sprint exercise, the actual development effort could not be measured in the same way as a real project. However, the estimates helped us distinguish between relatively complex requirements, such as emergency donor matching and preventing double allocation, and simpler requirements, such as recording donor responses. The exercise showed that story points are useful for comparing the relative effort of different requirements.

2. Was your backlog well-prioritized?

The backlog was prioritized according to the importance of the requirements. High-priority requirements related to emergency response, inventory accuracy, expiry management, and data integrity were given higher priority. Medium-priority requirements related to donor information and donor responses were planned accordingly.The most critical emergency blood matching and inventory-related requirements were included in Sprint 1, while donor management and security-related requirements were included in Sprint 2. This made the backlog organized according to the importance and dependency of the system features.

3. How did the simulated sprint align with your plan?

The sprint execution followed the planned backlog. Sprint 1 contained 4 stories and 21 story points, and all the planned stories were moved from To Do → In Progress → Done. After completing Sprint 1, Sprint 2 was started with 3 stories and 16 story points.All Sprint 2 stories were also moved through the workflow and completed successfully. Therefore, both sprints achieved their planned scope without leaving incomplete stories.

4. What insights did the Burndown Chart give about your team capacity?

The Burndown Chart helped us understand how the remaining work changed as stories were completed. A burndown chart compares completed work with the total work remaining and uses the ideal guideline to show whether the sprint is progressing at an appropriate rate.For our simulated sprint, the work reduced to zero because all planned stories were completed. Sprint 1 completed 21 story points, while Sprint 2 completed 16 story points. This exercise gave us an initial indication of the team's simulated capacity and showed how story points and sprint progress can be monitored using Jira.In a real project, the results from multiple completed sprints could be used to understand the team's velocity and improve future sprint planning.
